

Barnstable Town Council

Update on Wastewater Efforts In Barnstable

Department of Public Works
December 17, 2020




Update Since December



- **CWMP**
 - *MEPA Decision for Single EIR anticipated prior to the end of the calendar year.*
 - *After MEPA decision, petition Cape Cod Commission for 208 Consistency Determination.*
 - *Download document at:*
https://www.townofbarnstable.us/WaterResources/CWMP_Final.asp
- **JBCC**
 - *No new information*
- **Mothers Park**
 - *Continuing to work on road ownership issues*



Phasing Plan

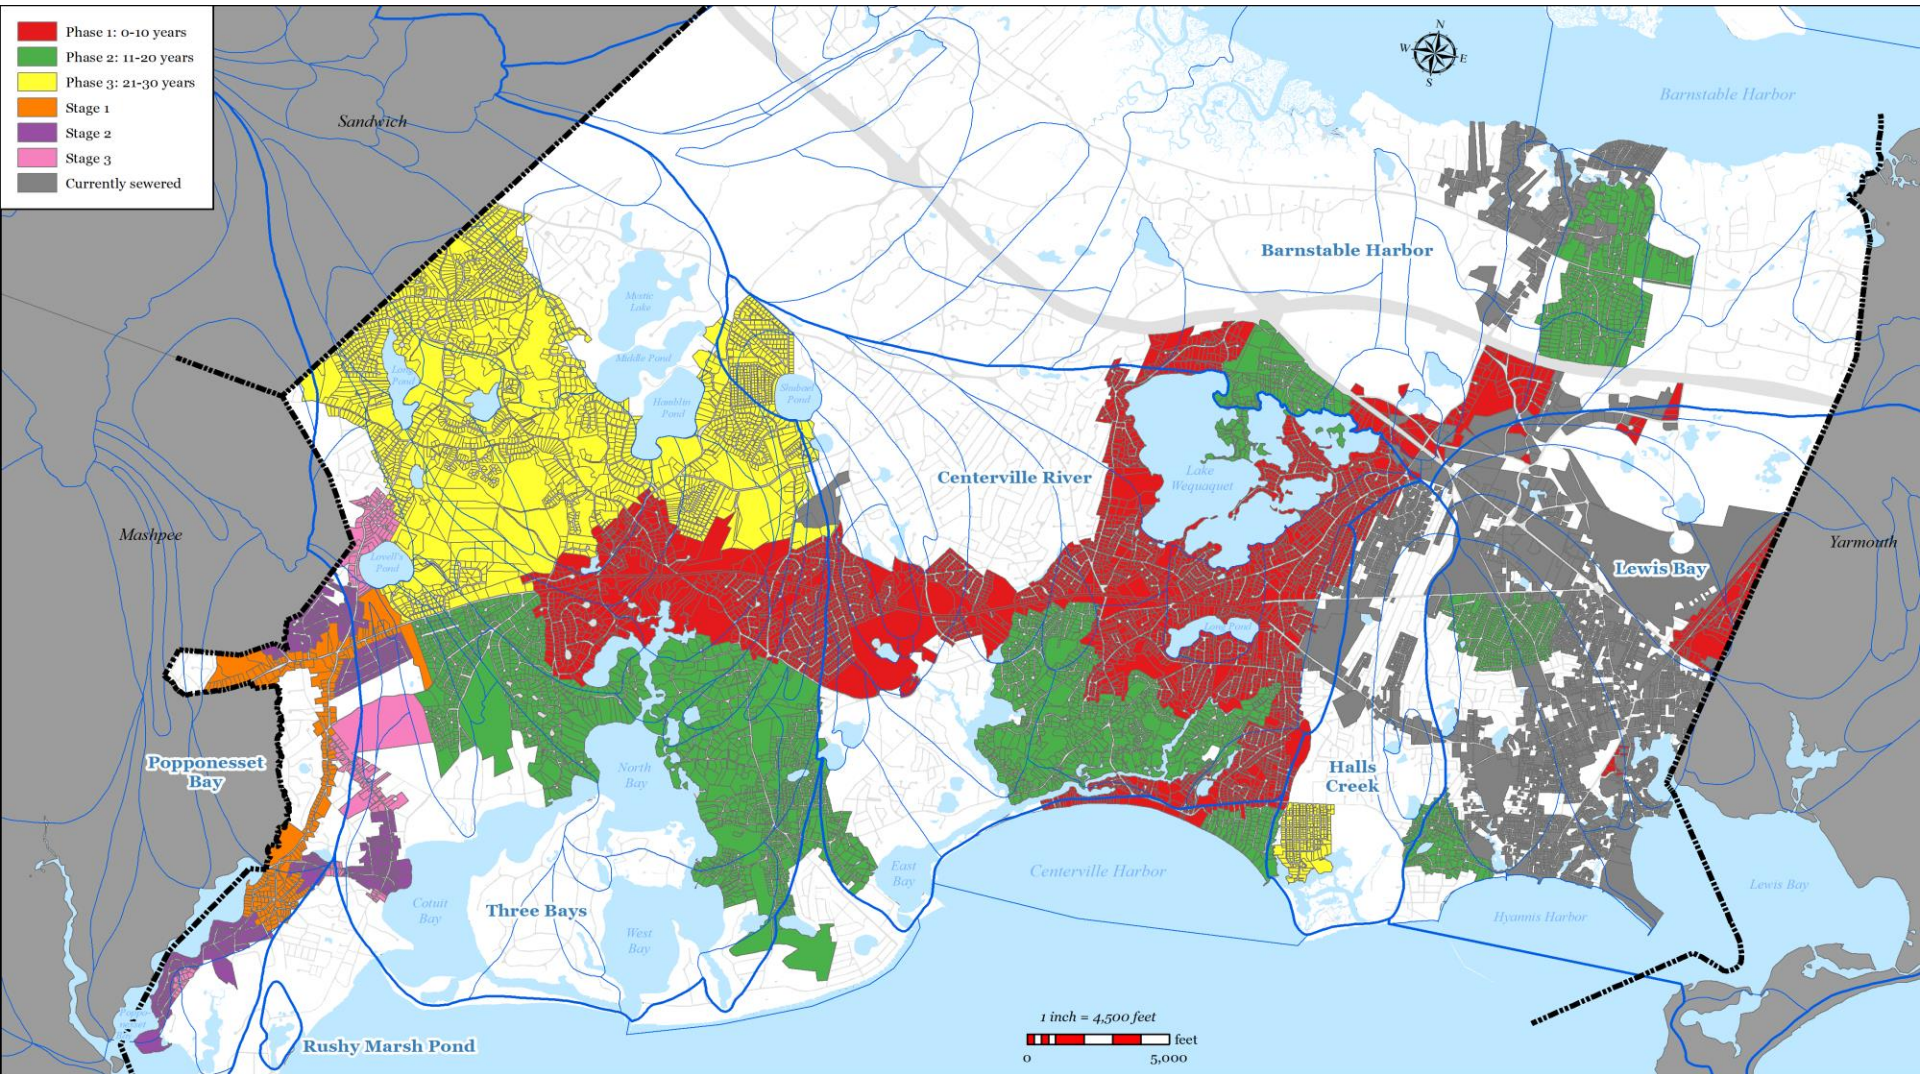



Update Since December




- **Projects**

- *Rte 28 East (pump station & Sewering at Phinney's Lane and 28)*
 - *Preliminary Design continues*
 - *Coordinating/partnering with Hyannis Water to remove “dead-ends” in water system as part of project.*
 - *Winter 2021/22 Construction Start Target*
- *Long Pond, Phinney Lane, and Rt 28 to Rt 149 survey commenced*
 - *Survey completion Target March 2021*
- *Strawberry Hill Road Project*
 - *Continuing design and coordination with Vineyard Wind designers*
 - *Coordinating construction sequencing plan with VW.*
 - *Spring anticipate water main relocations, sewer work likely starts in fall.*
 - *Pursuing opportunities for a more cost effective pump station site.*




Phase I Projects - East

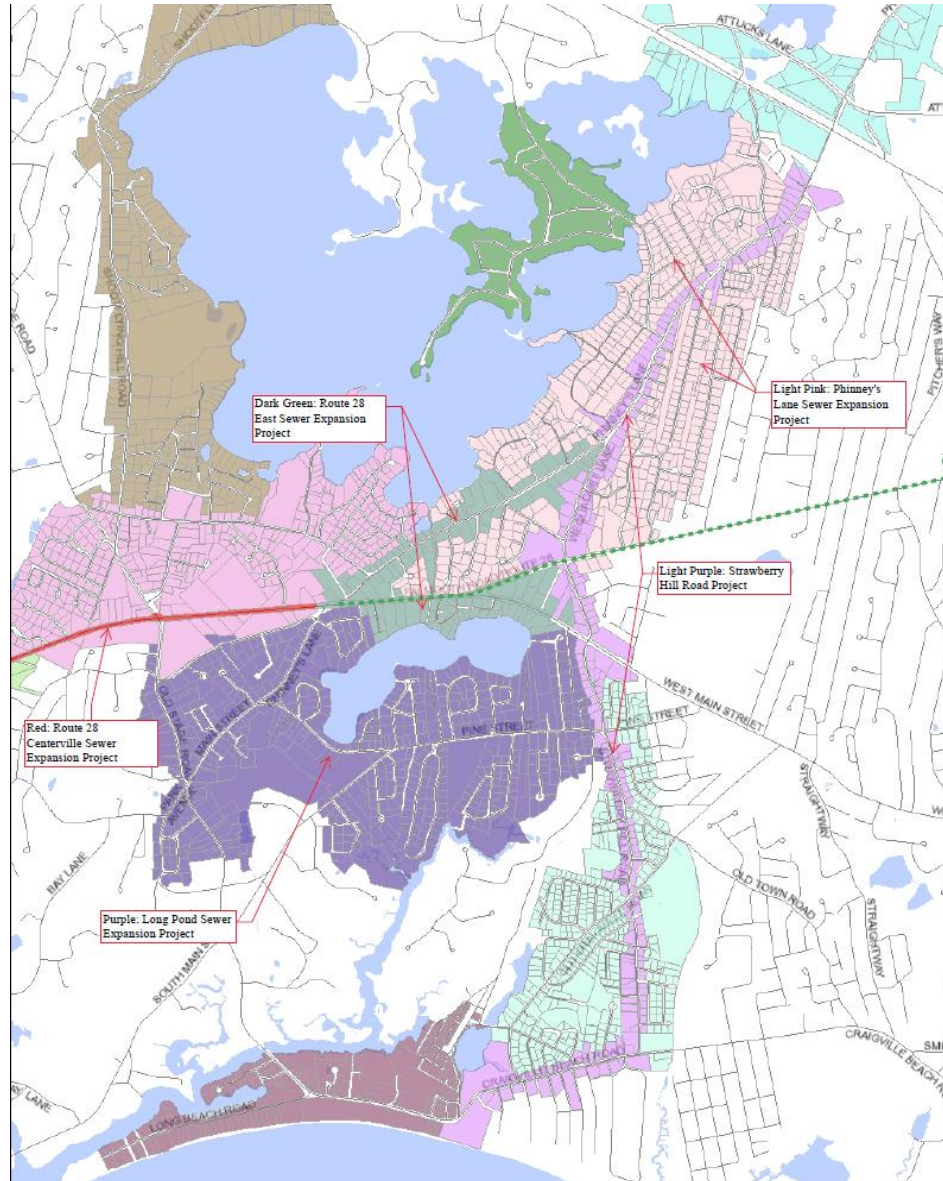



Phase I Projects - West

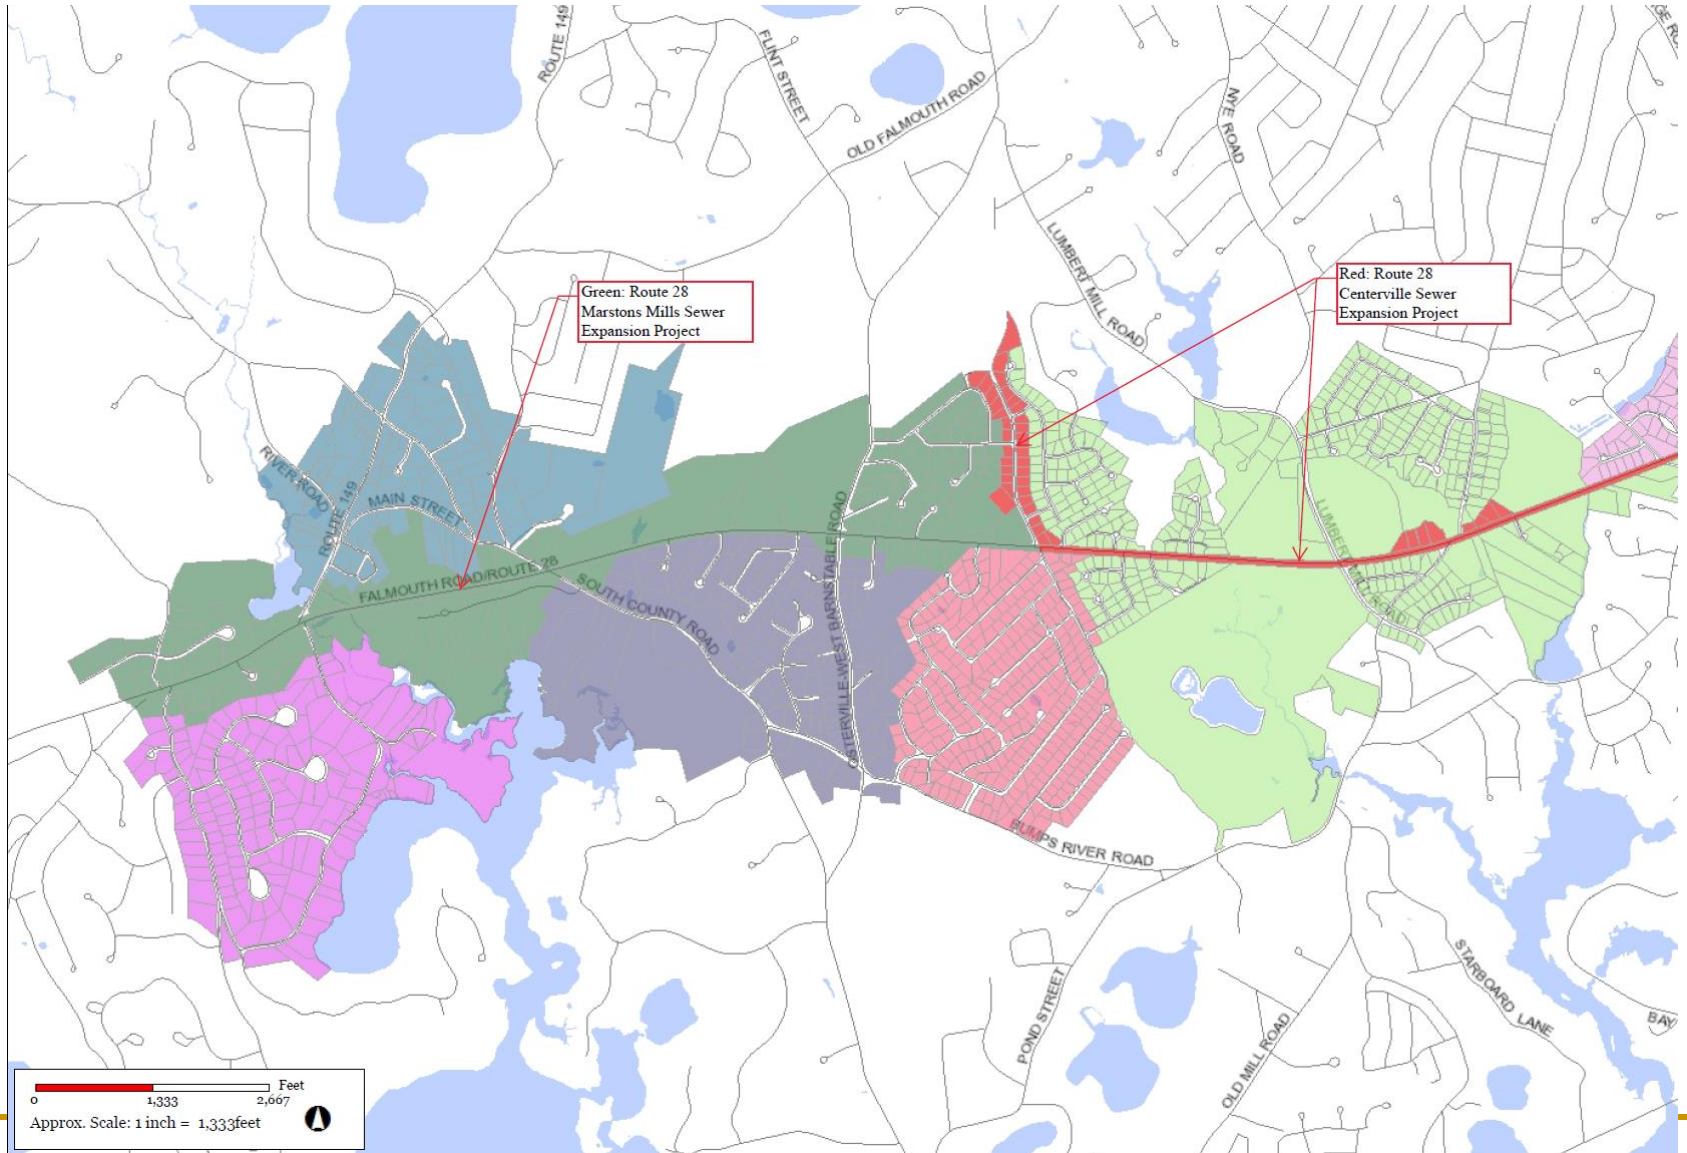



Discussion?

